# Lab 2: Jira Scrum Planning and Sprint Management

Software Engineering Lab | Jira project: SE Lab Submissions (SCRUM)

Project: https://akshayvr.atlassian.net/jira/software/projects/SCRUM

## Work completed

Created two epics and five user stories based on the Lab 1 coffee ordering system.
Stories include acceptance criteria, requirement traceability, priority, and Fibonacci estimates.
Planned two one-week sprints and moved all five planned stories through Done.

| Sprint | Goal | Stories | Planned | Done |
|---|---|---|---|---|
| Sprint 1 | Selection, customization, order review | SCRUM-7 to 10 | 10 pts | 10 pts |
| Sprint 2 | Payment and order confirmation | SCRUM-11 | 5 pts | 5 pts |

## Burndown summary

Planned story points remaining

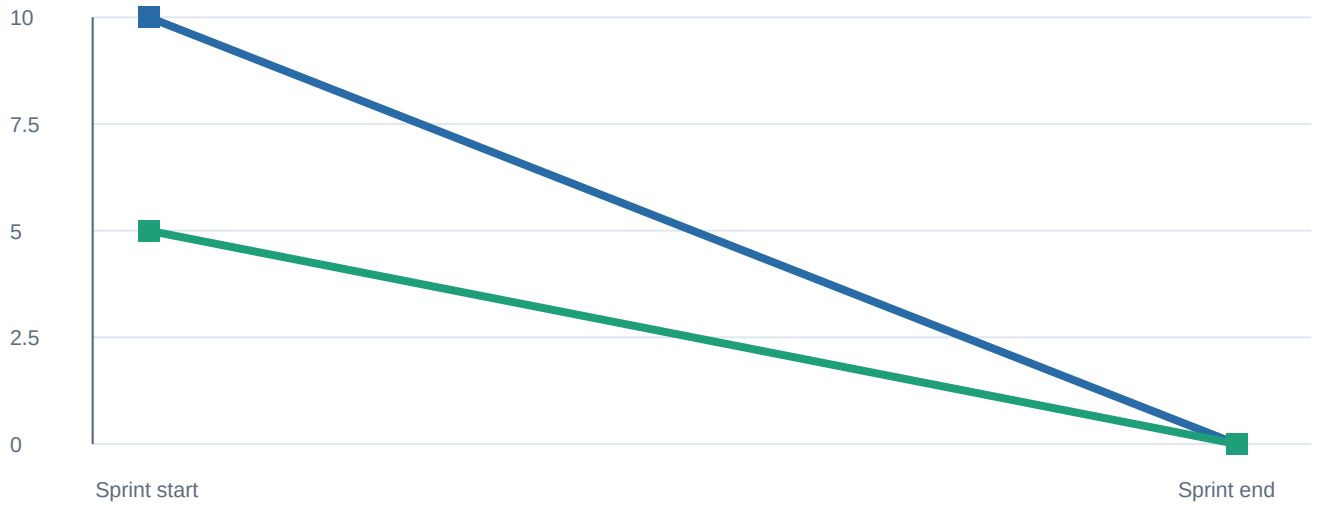


Sprint 1: 10 to 0 points

Sprint 2: 5 to 0 points

> Report note: Jira exposed a Sprint burndown chart option, but selecting it routed to a not-found page. This chart summarizes recorded sprint start/end totals; it is not an exported Jira report. Work was completed in one lab session, not day by day.

Evidence: Lab 2/evidence/jira-summary.jpg | Reflection answers on page 2

# Lab 2 Reflection

Jira Scrum planning and sprint management | SE Lab Submissions

## 1. How did planning help organize the work?

The backlog connected each customer-facing story to an epic and to the Lab 1 requirement it implements. Acceptance criteria made the expected behavior reviewable before work began. Sprint 1 grouped selection and order review; Sprint 2 held payment and confirmation. This made the planned scope and the remaining dependency visible.

## 2. What did story-point estimation add?

Fibonacci estimates gave the team relative sizes without pretending to know exact hours. The five stories were estimated at 3, 2, 3, 2, and 5 points. Payment received the largest estimate because of uncertainty around approval, decline, retry, and order creation. The two sprint loads were easy to compare: 10 points and 5 points.

## 3. How did the board workflow help?

The To Do, In Progress, and Done columns showed each story state and made completion visible. Moving stories across the board showed progress and made open work apparent when a sprint closed. All five planned stories reached Done; starter template issues were left out of the lab sprints.

## 4. What does the burndown show, and what are its limits?

The summary shows Sprint 1 going from 10 to 0 points and Sprint 2 from 5 to 0. Jira's report option routed to a not-found page, so the chart summarizes captured sprint totals instead of claiming to be an exported Jira report. All status transitions were done in one lab session, so the drop is concentrated at the start of each one-week window; it does not represent a realistic day-by-day work pace.
